


Re-New Platform: V1.0 Launch Guide

Following our January 18th alignment meeting

Platform Status & Launch Plan

This document summarizes our mid-January alignment on the Re-New platform. It covers current status, what's needed from each team member, and the timeline to go-live.

Summary: Platform development is 95% complete. The path to launch depends on finalizing the questionnaire content and a few configuration decisions.

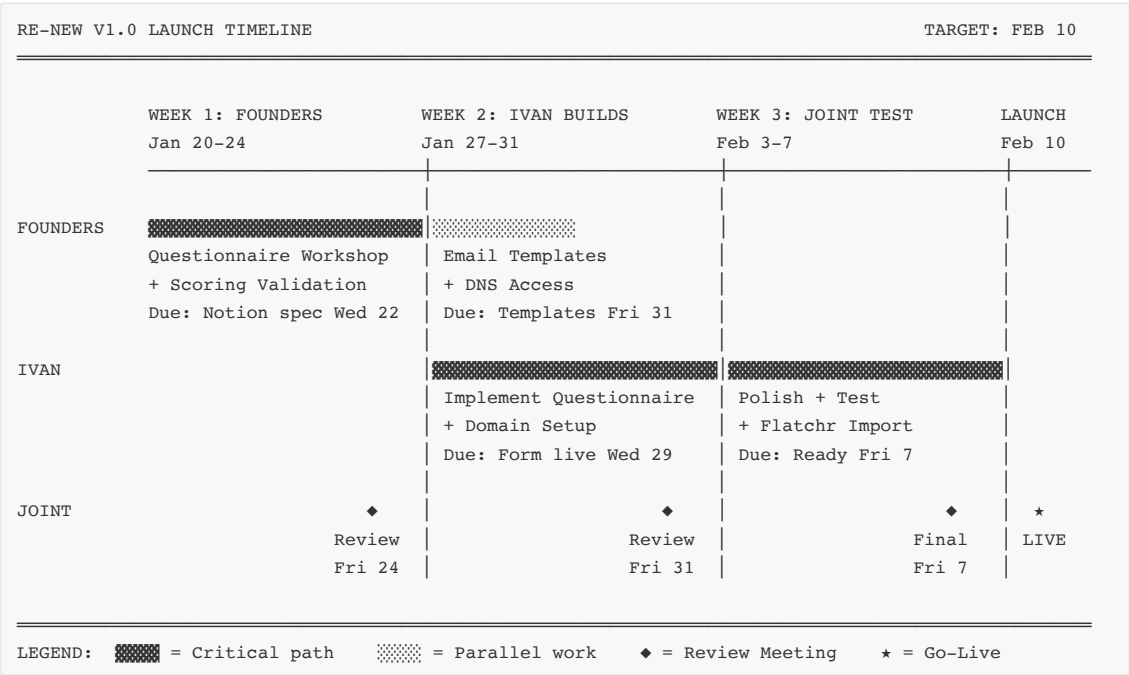

See detailed weekly breakdown at end of document.

Where We Are

Area	Status
Platform Infrastructure	DONE
Authentication System	DONE
Dashboard & CRM	DONE
Intake Form (tech ready)	Waiting for final question list
Email System (tech ready)	Waiting for templates
Scoring System	DONE
Logo on Intake Form	DONE
Custom URL	Pending DNS access

Platform status: 95% complete (36/38 tasks). All core features working. The blockers are content decisions, not code.

Where We're Going

Target: February 10th - Public launch of the intake questionnaire

A candidate visits `app.re-new.team/intake`, completes the questionnaire, and enters the Re-New pipeline. The team sees them in the dashboard, reviews their score, and begins the relationship.

This is V1.0: a professional, branded entry point that replaces ad-hoc candidate collection and establishes Re-New's digital presence.

The Critical Path

Everything flows from one decision chain:

Questionnaire Design --> Scoring Logic --> Journey Stages
(what to ask) (how to rank) (how to track)

Once founders finalize the questionnaire, Ivan implements it. The scoring weights follow from the questions. The journey stages follow from how candidates progress.

Three Workstreams for V1.0

Stream 1: Questionnaire Finalization

Owner: Bertrand + Amelie

Deadline: Wednesday, Jan 22nd

Why This Matters

The questionnaire is the highest-leverage decision in the entire launch. Every question you add creates friction. Friction loses candidates. A 20-question form that takes 15 minutes will lose 60% of applicants compared to a 10-question form that takes 5 minutes.

But you also need enough information to qualify leads. The tension is real.

What To Do

Finalize the question list in the Notion template. Three buckets:

1. **Basic data:** Name, email, phone. Non-negotiable.
2. **Profile quality:** Experience level, leadership history, M&A exposure. These determine if someone is a fit.
3. **Readiness indicators:** Have they done training? Secured funding? Have a Letter de Cadrage?

For Letter de Cadrage: if they have one, ask them to upload it (auto-scores 10 points). If not, skip those questions entirely.

Where To Be Careful

- **No questions requiring preparation.** If answering requires them to go find a document or think for 10 minutes, they'll abandon. Save those for follow-up conversations.
- **Once live, structure changes are costly.** Adding a question later is fine. Changing the fundamental data model is not. Get the buckets right now.

Deliverable: Complete the questionnaire template in Notion:

<https://www.notion.so/2ec36d8dca888099bd06e458acbbb554>

Stream 2: Email Templates

Owner: Bertrand + Amelie

Deadline: Friday, Jan 31st

Why This Matters

Emails are how you maintain the relationship after intake. But here's the strategic reality: this is a simple self-made CRM, not Mailchimp. The real email power will come from AI integration in V1.5, where the platform can draft personalized messages based on each candidate's profile.

For V1.0, the goal is simpler: **confirm templates work, test reliability, iterate.**

What To Do

Draft 5 email templates:

1. **Welcome Email** - after questionnaire submission
2. **Qualification Email** - when marked as "Qualified"
3. **Interview Invitation** - booking link
4. **Offer Proposal** - when offer assigned
5. **Follow-up Reminder** - if no response

HTML formatting is fine. Keep it clean: logo, clear text, one call-to-action per email.

Where To Be Careful

- **Don't over-engineer automation.** Manual sending is fine for the first 50 candidates. Focus on getting the content right, not the triggers.

- **Test deliverability.** Send test emails to different providers (Gmail, Outlook, corporate). Check spam folders.
- **Keep templates simple.** Complex HTML breaks in email clients. Logo + text + button is enough.

Stream 3: Domain & Branding

Owner: Bertrand (DNS) + Ivan (setup)

Deadline: Friday, Jan 31st

Why This Matters

The intake form is the first impression of Re-New's digital presence. A URL like `v0-re-new-2-0.vercel.app` looks amateur. `app.re-new.team` signals professionalism.

This is the facade. What candidates see before they've decided to engage.

What To Do

Item	Status
Logo on intake form	DONE
Custom domain (app.re-new.team)	Pending - Bertrand to provide DNS access

For domain setup: Bertrand logs into domain registrar (OVH, Gandi, Cloudflare) and either shares access with Ivan OR adds CNAME record: `app` pointing to `cname.vercel-dns.com`. Ivan handles the rest.

Where To Be Careful

- **DNS changes take time to propagate.** Do this early in the week, not Friday.
- **SSL certificate activates automatically** once DNS is configured. No action needed.

Stream 4: Platform Consolidation

Owner: Bertrand + Amelie (review) + Ivan (implementation)

Deadline: Friday, Jan 31st

Why This Matters

The platform was built based on assumptions about how Re-New works. Some of those assumptions need validation. Before going live, founders should scrutinize what exists and decide: keep as-is, refine, or remove.

This is as important as the questionnaire. The questionnaire defines what data comes IN. This stream defines how that data is USED.

What To Do

1. Milestone Definitions (Priority)

The platform tracks candidates through journey stages with milestones. Current stage names and milestone definitions may not match how Re-New actually thinks about the candidate journey.

Review and confirm:

- Are the stage names right? (Lead → Qualified → Client)
- Are the milestones meaningful? (First call done, Letter de Cadrage received, etc.)
- Should milestone validation be manual or automatic?

Recommendation: Keep milestone validation MANUAL (human clicks checkbox). Even for file uploads like LDC, manual review is safer. Effort is minimal (one click) but prevents automation errors and maintains quality control.

2. Feature Evaluation

Some features were built as drafts and need validation. For each, decide: useful as-is, needs refinement, or remove entirely.

Feature	Current State	Decision Needed
Notes system	Basic (call/email/meeting types)	Keep/Refine/Remove?
Activity tracking	Logs all actions	Useful or noise?
Offers system	Links offers to candidates	Matches your workflow?

It's OK to leave everything unchanged. But if something doesn't fit how you actually work, better to know now than after launch.

Where To Be Careful

- **Don't overthink it.** If unsure, keep the feature. You can always remove later.
 - **Test with real scenarios.** Walk through an actual candidate journey in the platform during Week 3.
-

AI Intelligence (V1.5 - After Launch)

Owner: Ivan
Status: Waiting for Anthropic account
Budget: \$100 initial (one-time to assess costs and experiment)

What AI can enable:

- Automated scoring of CV/Letter de Cadrage uploads
- AI-drafted personalized emails based on candidate profile
- Smart matching between candidates and offers

Strategic Note: AI is explicitly V1.5. Don't wait for it to launch V1.0. The platform works today without AI. The intelligence layer is an enhancement, not a requirement.

Founders' action: Create Anthropic account, add payment method, share login credentials with Ivan. Ivan extracts API keys, experiments, and returns with cost estimates.

Operational Coordination

For coordinating and orchestrating at an operational level, I have created a task list directly on the Re-New platform:

[View Tasks on Platform](#)

Why on the platform? So we can all user-test it together: authorization flows, platform capabilities, email automation, and general functionality. This reduces the chance of errors when real users arrive.

This document provides strategic context. The task system provides operational execution.

After V1.0

Once V1.0 is live and stable, two directions open up.

AI Intelligence (V1.5)

With the Anthropic account in place, we'll quickly experiment with adding intelligence to the platform. The goal is to test costs and benefits: Can AI meaningfully score uploaded documents? Can it draft personalized emails that save time without losing quality? This is exploratory work. We'll run small experiments, measure what works, and decide what to productize.

Major Platform Expansions (V2.0+)

Larger opportunities exist but require separate strategic discussion. These don't impact V1.0 and will be addressed in their own planning cycle:

- **Opening to intermediaries:** An anonymized portal where M&A brokers can browse qualified candidates. This turns Re-New's qualification work into a visible, sellable asset.
- **Opening to candidates:** A self-service layer where entrepreneurs access training resources, track their own progress, or browse available deals.
- **Deal marketplace:** Sellers post opportunities, candidates browse and express interest, Re-New facilitates matching.

Each of these is a significant product decision with its own timeline, costs, and strategic implications. They will be discussed when V1.0 proves stable and the team has bandwidth to think bigger.

Reference Documents

- **Questionnaire Template (Notion):** <https://www.notion.so/2ec36d8dca888099bd06e458acbbb554>
- **Task Management (Platform):** <https://v0-re-new-2-0.vercel.app/tasks>
- **Current Platform:** <https://v0-re-new-2-0.vercel.app>
- **Re-New Website:** <https://re-new.team>

Detailed Weekly Breakdown

DETAILED WEEKLY BREAKDOWN	
WEEK 1: FOUNDERS DEFINE	Jan 20–24

TIMELINE	Mon 20 Workshop Starts	Tue 21	Wed 22 SPEC DUE	Thu 23	Fri 24 REVIEW MEETING	
DELIVERABLES			DUE	OWNER	STATUS	NOTES
Questionnaire spec (Notion template) path			Wed 22	B+A	☐	Critical
Scoring weights validated implementation			Wed 22	B+A	☐	For
Journey stage names confirmed meeting			Fri 24	B	☐	Review in
LDC handling decision uploaded			Wed 22	B+A	☐	10 pts if
◆ CHECKPOINT Fri 24: Review meeting – Confirm spec complete, ready for Ivan to implement						
WEEK 2: IVAN BUILDS						Jan 27–31
TIMELINE	Mon 27 IMPLEMENT STARTS	Tue 28	Wed 29 DOMAIN LIVE	Thu 30	Fri 31 REVIEW MEETING	
DELIVERABLES			DUE	OWNER	STATUS	NOTES
Questionnaire implemented spec			Wed 29	Ivan	☐	Based on
Domain app.re-new.team configured access			Fri 31	Ivan	☐	Needs DNS
Welcome email automation format			Fri 31	Ivan	☐	Plain text
DNS access provided Vercel			Mon 27	B	☐	CNAME to
Email templates drafted needed			Fri 31	B+A	☐	5 templates
Flatchr CSV exported import			Fri 31	B	☐	For Week 3
◆ CHECKPOINT Fri 31: Review meeting – Confirm form live and working on custom domain						
WEEK 3: JOINT TESTING						Feb 3–7
TIMELINE	Mon 3 FLATCHR IMPORT	Tue 4	Wed 5 USABILITY TESTS	Thu 6	Fri 7 FINAL CHECK	
DELIVERABLES			DUE	OWNER	STATUS	NOTES
Flatchr historical data imported export			Mon 3	Ivan	☐	From CSV
Intake form usability tested flow			Wed 5	B+A	☐	Test full
Email automation verified emails			Wed 5	Ivan	☐	Send test
Journey stages reviewed names			Thu 6	All	☐	Confirm
Notes/Activity features validated remove?			Thu 6	All	☐	Keep or

All issues fixed
polish

Fri 7

Ivan



Final

◆ CHECKPOINT Fri 7: Final sign-off from Bertrand – Ready for go-live

GO-LIVE: FEBRUARY 10

★ ★ ★

GO-LIVE CHECKLIST

STATUS

Questionnaire live and tested on app.re-new.team/intake



Domain app.re-new.team working with SSL certificate



Welcome email sends correctly after form submission



Flatchr historical candidates imported into platform



Team trained on dashboard usage



Final sign-off from Bertrand

